



February 20, 2023

Peters Township Municipality
610 East McMurray Road
McMurray, PA 15317

RE: Valley Brook Road/Bebout Road Intersection Improvement Project - ECMS# 109242

ATTN:


We have been awarded the above referenced contract from PennDOT.

This project consists:

The project area is in Peters Township, Washington County. The existing SR 1010 (Valley Brook Road) and SR 1019 (Bebout Road) intersection is a stop-controlled, T intersection. SR 1010 serves as the primary commuter connection to US 19 and the larger Pittsburgh region. The needs of the project include capacity deficiencies and inadequate pedestrian and ADA accommodations. The primary purpose of this project is to relieve congestion and queuing, improve safety, enhance access to the adjacent trail, and expand the bicycle and pedestrian network. Minor strip takes of right-of-way are anticipated.

This project being situated as follows:

From Valley Brook Road (SR 1010) at Segment 0190 Offset 1407 (Station 104+00) eastbound to the intersection at Bebout Road (SR 1019) Segment 0070 Offset 0000 (Station 200+00). Bebout Road (SR 1019) at Segment 0070 Offset 0350 (Station 203+50) Northbound and Segment 0190 Offset 2182 (Station 111+75) Southbound of intersection.

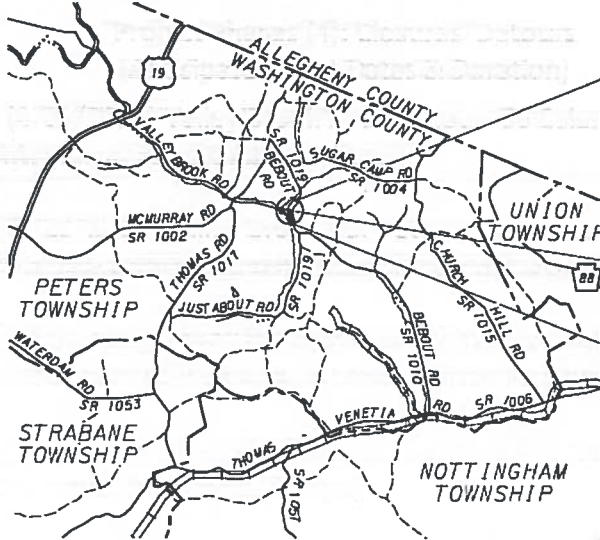

Project Phases (4): Closures/Detours
(Anticipated Start Dates & Duration)

- Phase 1** - (4/03/2023) Valley Brook Road Detour- 66 Calendar Days. (Utilizing McMurray Road to Bebout Road)
- Phase 2** - (5/23/2023) Valley Brook Rd. Detour Continues - Bebout Rd reduced to Single Lane using Temporary Traffic Signals (19 Days).
- Phase 3** - (6/30/2023) Valley Brook Rd Opens/ Bebout Rd Detour Begins (35 Days). (Utilizing Valley Brook Rd to McMurray Rd to Bebout Rd)
- Phase 4** - (7/17/2023) Bebout Rd Detour Continues/ Temporary Traffic Signals used South Bebout Rd (9 Days)

Total Anticipated Duration (215 Calendar Days)

Thank you,



Caleb Schultz
Project Manager
FOLINO CONSTRUCTION, INC.
